

**CITY OF EAST PROVIDENCE  
WATER UTILITIES DIVISION  
FLOW TEST REPORT**

Location: CRESCENT VIEW AVE (BULLOCKS Pt. VILLAGE) Date: 9/21/2021  
Test Made By: JUSTIN ST. ONGE Time: 10:00 AM  
Representative of: JOE CASALI ENGINEERING  
Witnessed By: CITY OF EAST PROV. - WATER DEPT. ST. M. ROYAL  
State Purpose of Test: FIRE PROTECTION


Hyd. #	<u>912</u>	Static	<u>78</u> psi	Residual	<u>70</u> psi
		Hyd. #		Hyd. #	
Flow Hydrants:	<u>916</u>				
Size Nozzle	<u>2 1/2"</u>				
Pitot Reading	<u>61</u>				<u>Total GPM</u>
GPM	<u>1310</u>				

Consumption Rate During Test: \_\_\_\_\_


Size of Main in Street: 12"

Remarks: \_\_\_\_\_


Location Map: Show line sizes and distance to next cross connected line. Show valves and hydrant branch size. Indicate North. Show flowing hydrants. Show location of Static and Residual hydrants.

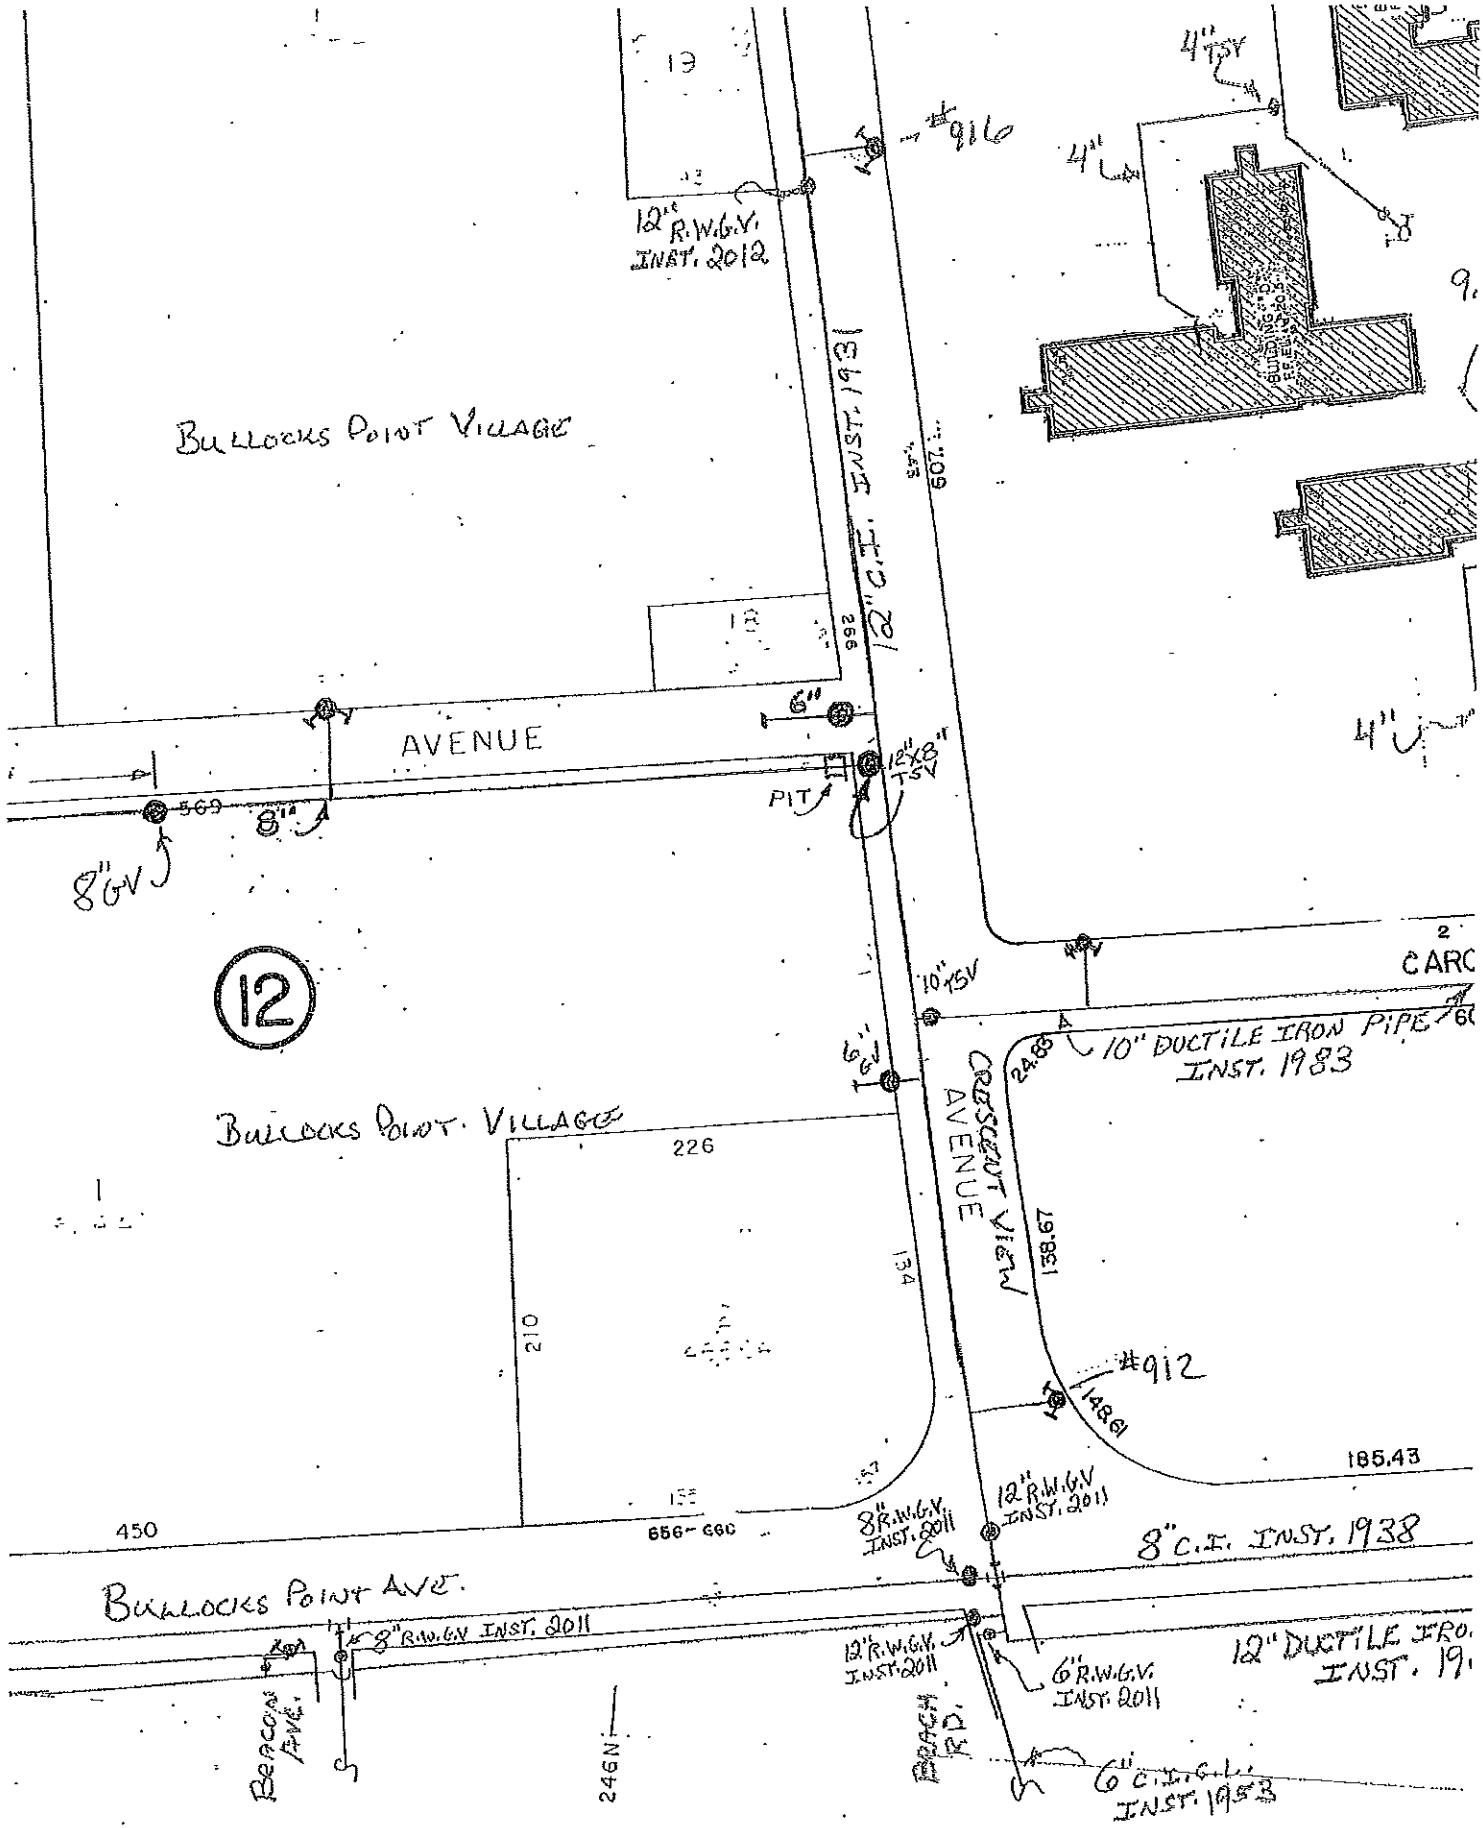

12



1" = 100'



REVISION	
NO.	DATE
TC-1	12-97
